



VCL PMO System

A single, plain-English status pack for the project we are using to build the system that runs all our other projects.

PROJECT ID	SPONSOR	PHASE
VCL-DEV-PMO-002	Tanuj Haria	Phase 2 – Build
STARTED	TARGET FINISH	THIS REPORT
27 May 2026	7 June 2026	28 May 2026

Where we are today

Status as at 21:30 EAT, 28 May 2026.

DONE

2

work blocks shipped

IN FLIGHT

1

waiting on one
setup step

WAITING

1

design write-up
pending

HEALTH

On track

target 7 Jun stands

One sentence: The PMO is being built inside ERPNext as the new home for all VCL development work – so plans, tasks, agents, testing and approvals all live in one place. As of today, four of the four planned work blocks are either shipped or coded; the only remaining steps before the system is end-to-end operational are one Slack token install and one design write-up.

What we just finished

WHAT	WHY IT MATTERS	STATUS
Back button works everywhere	Pressing browser Back from any sub-page now returns to the right tab instead of landing on a "page not available" error. Reload and pasted links also work.	• DONE
Tests are grouped by what they test	Instead of one long flat list of UAT/OAT items, each shift's tests sit under a clear header showing pass/fail/blocked counts. Easier to walk through, easier to sign off.	• DONE

What is built but waiting on one setup

WHAT	WHY IT MATTERS	WHAT IT NEEDS
Plans go to Slack as PDFs	One click renders any plan as a clean, A4, VCL-branded PDF and drops it in #ai-pmo-plans. Sized for reading and annotating on reMarkable or Boox Air 5.	Install a Slack bot token in the site settings, invite the bot to the channel. About 10 minutes of admin.

What is still on the drawing board

WHAT	WHY IT MATTERS	OWNER
Auto-review of new plans by agents	Today every new plan needs Tanuj to manually choose Claude / Codex / human for each item. The design will let an agent draft the proposed allocation overnight and send Tanuj a single Approve button.	Codex — design only, not code, by 30 May



How it works – the buttons in order

The whole system is driven by six buttons in the PMO page at /app/pmo. Navy = primary action; amber = brand action; outline = secondary.

01 Open /app/pmo and pick the project

VCL PMO System

Lands on the project page with all the tabs across the top.

02 Plans tab – start a new plan

+ New Plan

Modal opens. You type a title + description, click Save.

03 Add items to the plan

+ Add Item

Each item picks a type (Shift, Task, Milestone, RAID...).

04 Push the plan to Slack as a branded PDF

Send PDF to Slack

Lands in #ai-pmo-plans, reads cleanly on reMarkable.

05 Tick items, allocate to an agent or human

Allocate to Claude

Allocate to Codex

Allocate to Human

Items become Shifts. Each Shift auto-creates its UAT/OAT records, bucketed under the shift.

06 Send the shift to the agent

Execute via n8n

Agent picks it up, works, commits, then calls Complete back into ERPNext.

Figure 1. The six clicks from idea to running shift.

Then the agent loop fires

Once a shift is dispatched, the rest of the cycle runs without you. Each lane below is one actor; arrows show the handover.

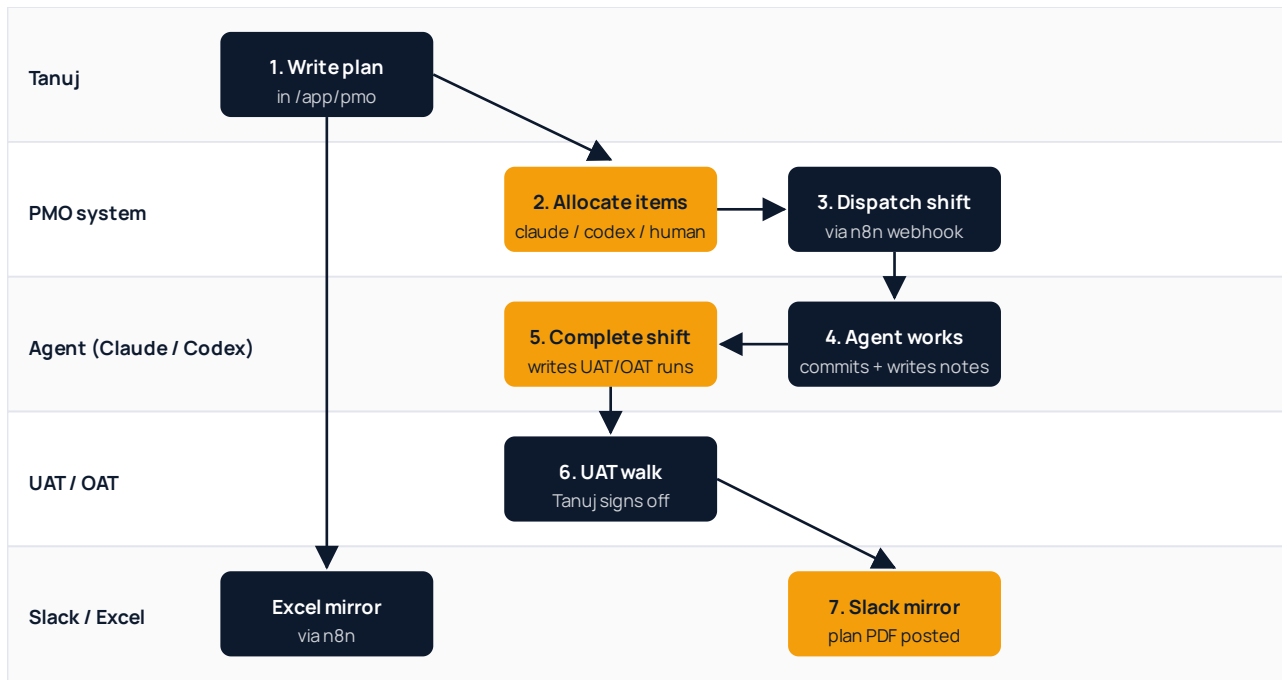


Figure 2. One full loop from plan to signed-off tests, mirrored to Slack and Excel.

Where each piece lives

We deliberately do *not* try to put everything in one tool. The principle is two anchors: ERPNext is the operational source of truth for project work, and Slack + Excel exist as downstream review surfaces that already work for the team.

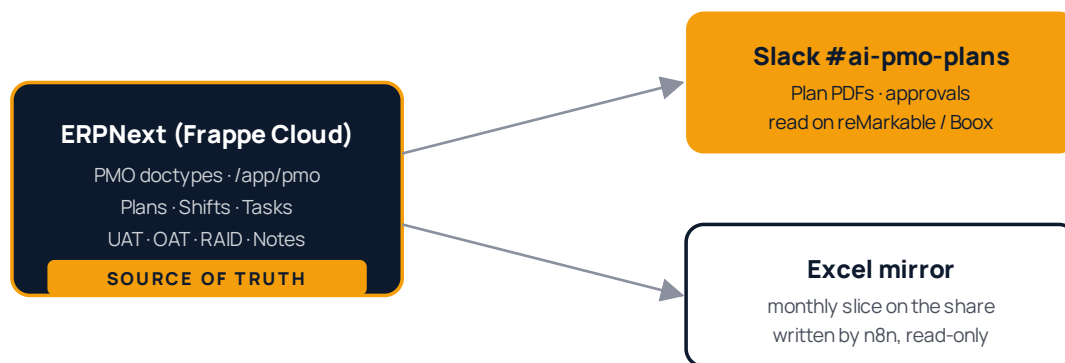



Figure 3. One source of truth, two downstream review surfaces. No reverse writes from Slack or Excel back into ERPNext.

What that means in practice

- **You edit in ERPNext.** Everything else mirrors automatically.
- **Slack is for reading and annotating.** Plans land there as PDFs; nothing in Slack writes back.
- **Excel is for the monthly slice.** n8n writes a workbook per project on the share; you never edit it directly.
- **Agents talk to ERPNext directly** via whitelisted API methods. n8n is the routing layer, not a data store.

Visual reference

The PMO interface inside ERPNext follows a deliberate style language. These are the two mockups we built before settling on a direction. The live system follows the **Mix A – Steel** palette: light surface, navy frame, amber accents.

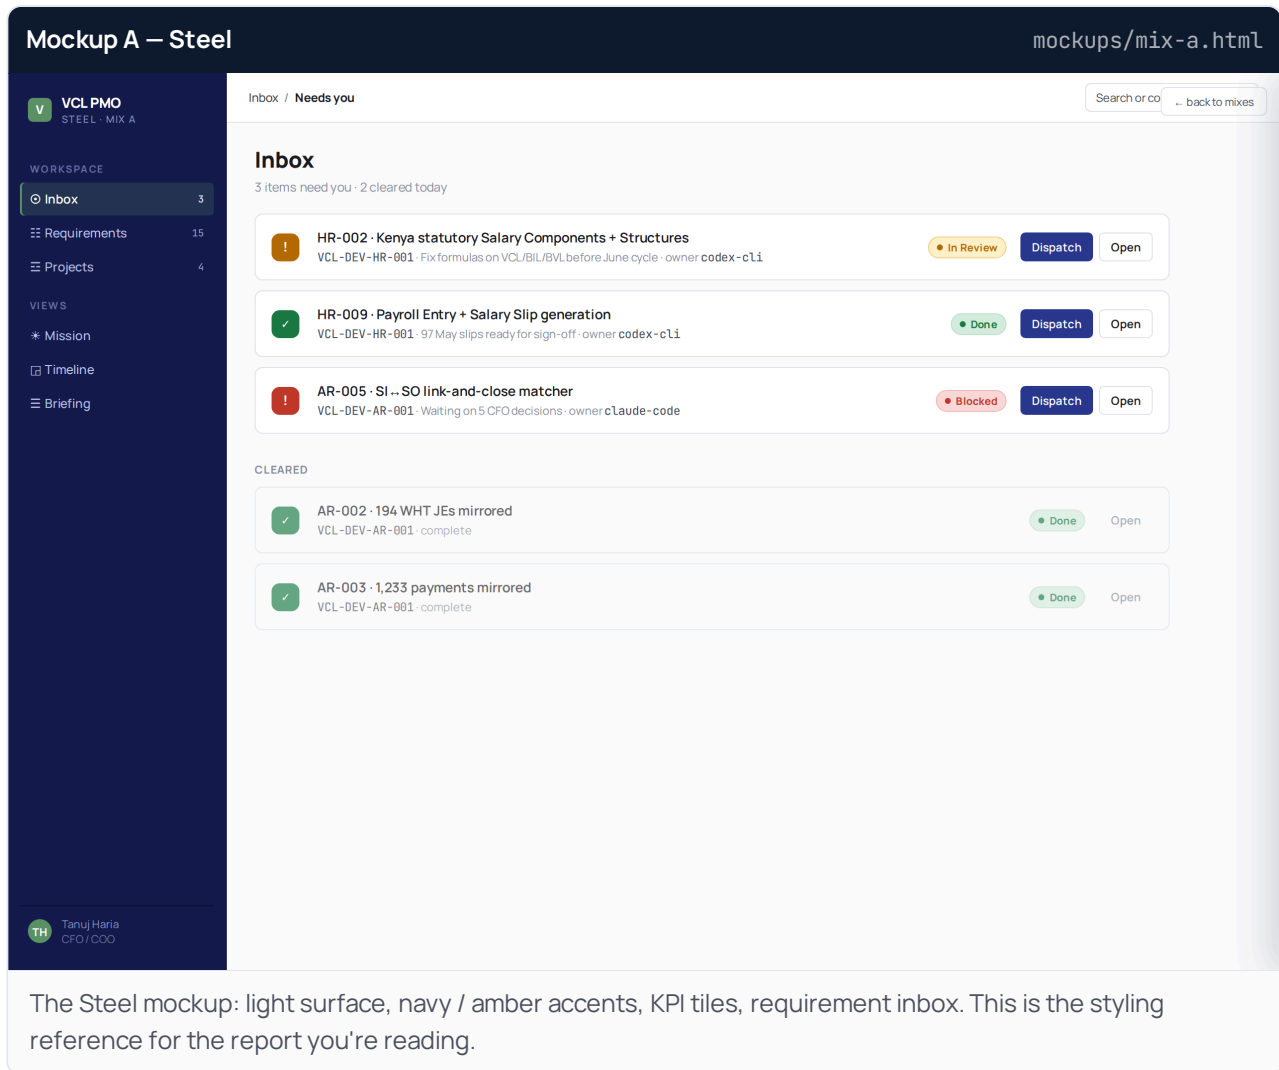

• LIVE UTC 18:49:32 HR-PAYROLL LIVE SLIPS 97 VARIANCE 0.49% HR-002 IN REVIEW AR-005 BLOCKED DONE 10/15

mixes



VCL PMO
PULSE · MIX C

Mission

Queue

Requirements

Timeline

Briefing

Search · command

K

TH

ACTIVE PROJECTS

+1 BUILD

3 /4

HR live · IMP active · AR active



REQUIREMENTS DONE

10

of 15 · 66.7%



NEEDS ACTION

3

in your queue



BLOCKED

1

AR-005 · CFO decisions




PROJECTS

REALTIME

HR & Payroll Module

VCL-DEV-HR-001 · ERPNext v16 + FastAPI
Intranet



100%

LIVE



VCL PMO System

VCL-DEV-PMO-002 · FastAPI + SQLite +
ERPNext links



15%

IN BUILD



Imports Portal

VCL-DEV-IMP-001 · Frappe custom app



25%

ACTIVE



ERP--QBO AR Alignment

VCL-DEV-AR-001 · Finance reconciliation



60%

ACTIVE



ACTIVITY FEED

07:45

codex-cli marked HR-002 → In Review

06:30

system dispatched HR-002 → agent

06:12

codex-cli marked HR-009 → Done

Yesterday

17:00

tanuj approved HR-011

Yesterday

16:20

claude-code marked IMP-001 → Done

The Pulse mockup: dark theme, live ticker, sparkline KPIs. Alternate visual treatment proposed but not built into /app/pmo yet.



What comes next

Before this Friday (29–30 May)

OWNER	ACTION	BY
<i>Tanuj</i>	Install a Slack bot in the workspace, drop its token into the PMO site settings, invite it to #ai-pmo-plans .	29 May
<i>Tanuj</i>	Walk the back-button fix on three real flows (Plans → Plan, Shifts → Shift, UAT case detail). Sign off SHIFT-0001.	29 May
<i>Tanuj</i>	Once the bot is in: click Send PDF to Slack on one plan. Confirm it lands and reads cleanly on reMarkable. Sign off SHIFT-0003.	29 May
<i>Codex</i>	Write the spec for "auto-review of new plans" — six points, no code. Lands as a markdown doc in the repo.	30 May

Following week (2–7 June)

OWNER	ACTION	BY
<i>Tanuj</i>	Review the auto-review spec, mark it Pass, hand off to Claude or Codex to build.	2 Jun
<i>Tanuj</i>	Close the Phase 2 Foundation milestone (MS-PMO-001). System officially the master for development work.	3 Jun
<i>Claude or Codex</i>	Build the scheduled plan-review job (nightly sweep, capacity-aware routing, single approve action).	5 Jun
<i>Tanuj</i>	UAT the scheduled job end-to-end. Mark project Done.	7 Jun

Open questions for Tanuj

Q1. Slack bot — create a new one called *VCL PMO Bot*, or reuse an existing workspace bot? (Recommend new, so scopes stay minimal.)

Q2. Auto-review trigger — every 6 hours, nightly at 23:00, or hourly when an unallocated plan appears? (Recommend nightly 23:00.)

Q3. Capacity probe for Codex — manual flag in site settings, or external monitor file?
(Recommend manual flag this round.)

Q4. Where do approvals live — Slack with a button, Telegram with a reply, or just the Plans tab?
(Recommend Slack with a permalink back to /app/pmo.)

Tanuj Haria — Sponsor

Date

