

VCL PMO System

A single, plain-English status pack for the project we are using to build the system that runs all our other projects.

PROJECT ID	SPONSOR	PHASE
VCL-DEV-PMO-002	Tanuj Haria	Phase 2 – Build
STARTED	TARGET FINISH	THIS REPORT
27 May 2026	7 June 2026	28 May 2026

Where we are today

Status as at 21:30 EAT, 28 May 2026.

DONE

2

work blocks shipped

IN FLIGHT

1

waiting on one
setup step

WAITING

1

design write-up
pending

HEALTH

On track

target 7 Jun stands

One sentence: The PMO is being built inside ERPNext as the new home for all VCL development work – so plans, tasks, agents, testing and approvals all live in one place. As of today, four of the four planned work blocks are either shipped or coded; the only remaining steps before the system is end-to-end operational are one Slack token install and one design write-up.

What we just finished

WHAT	WHY IT MATTERS	STATUS
Back button works everywhere	Pressing browser Back from any sub-page now returns to the right tab instead of landing on a "page not available" error. Reload and pasted links also work.	• DONE
Tests grouped by what they test	Instead of one long flat list of UAT/OAT items, each shift's tests sit under a clear header showing pass/fail/blocked counts. Easier to walk through, easier to sign off.	• DONE

Built but waiting on one setup step

WHAT	WHY IT MATTERS	WHAT IT NEEDS
Plans go to Slack as PDFs	One click renders any plan as a clean, A4, VCL-branded PDF and drops it in #ai-pmo-plans. Sized for reMarkable / Boox.	Install a Slack bot token in the site settings, invite the bot to the channel. About 10 minutes of admin.

↓
How do we
do this ?

Still on the drawing board

WHAT	WHY IT MATTERS	OWNER
Auto-review of new plans by agents	Today every new plan needs Tanuj to manually choose Claude / Codex / human per item. The design will let an agent draft the proposed allocation overnight and send Tanuj a single Approve button.	Codex — design only, by 30 May



How it works – the buttons in order

The whole system is driven by six buttons in /app/pmo. Blue = primary action; amber = warning / brand action; sage = brand accent; outline = secondary.

01 Open /app/pmo and pick the project

VCL PMO System

Lands on the project page with all the tabs across the top.

02 Plans tab – start a new plan

+ New Plan

Modal opens. You type a title + description, click Save.

03 Add items to the plan

+ Add Item

Each item picks a type (Shift, Task, Milestone, RAID...).

04 Push the plan to Slack as a branded PDF

Send PDF to Slack

Lands in #ai-pmo-plans, reads cleanly on reMarkable.

05 Tick items, allocate to an agent or human

Allocate to Claude

Allocate to Codex

Allocate to Human

Items become Shifts. Each Shift auto-creates its UAT/OAT records, bucketed under the shift.

06 Send the shift to the agent

Execute via n8n

Agent picks it up, works, commits, then calls Complete back into ERPNext.

Figure 1. The six clicks from idea to running shift. Colours match the deployed UI.

Then the agent loop fires

Once a shift is dispatched, the rest of the cycle runs without you. Each lane is one actor; arrows show the handover.

What does the agent do &
how does it fire up?

? What about new projects?

who approves this?

how are these linked?

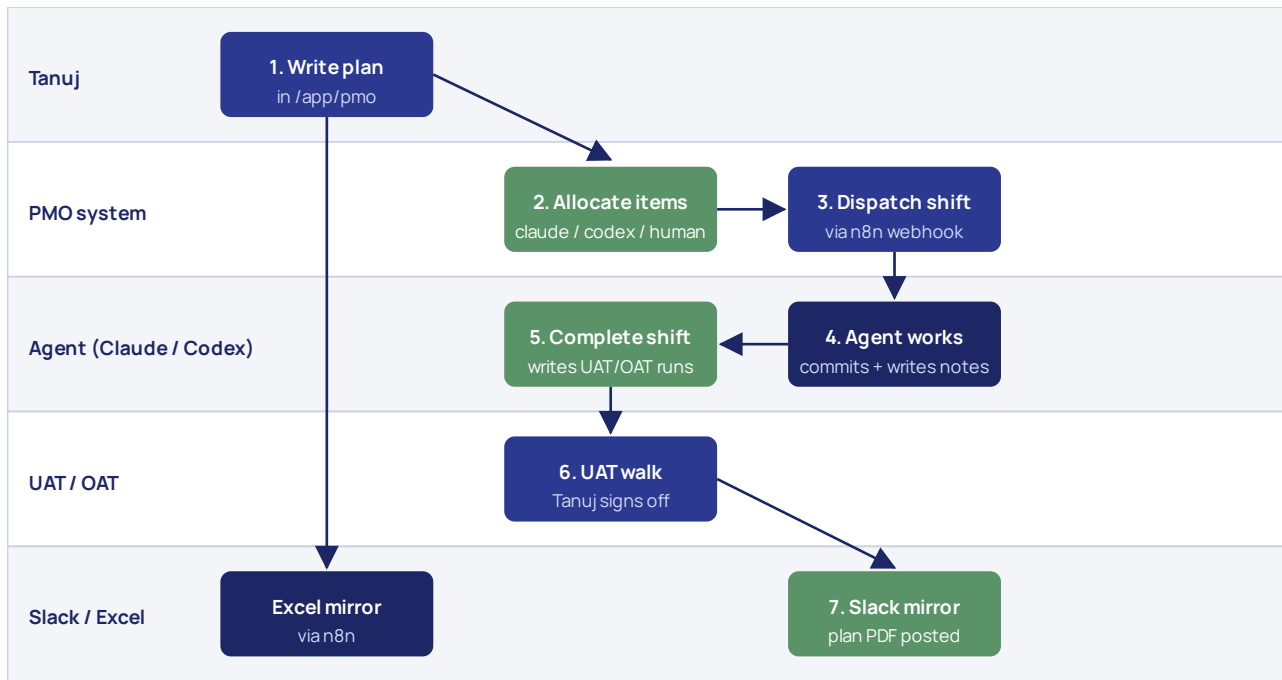


Figure 2. One full loop from plan to signed-off tests, mirrored to Slack and Excel.

Tanuj will add a rough plan, or what direction we want to go in.

↓

Read by codex or claude depending on tokens & usage they draft & send a plan to Tanuj via Slack for approval.

Where each piece lives

We deliberately do *not* try to put everything in one tool. Two anchors: ERPNext is the operational source of truth, Slack + Excel are downstream review surfaces that already work for the team.

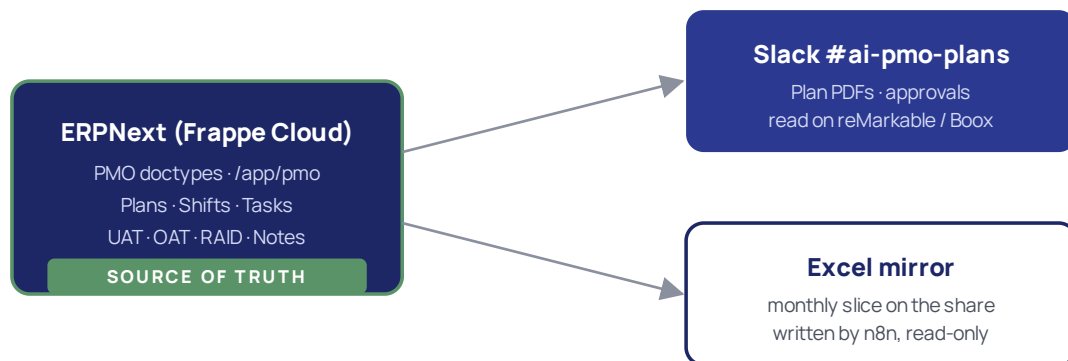


Figure 3. One source of truth, two downstream review surfaces. No reverse writes from Slack or Excel back into ERPNext.

What that means in practice

- **You edit in ERPNext.** Everything else mirrors automatically.
- **Slack is for reading and annotating.** Plans land there as PDFs; nothing in Slack writes back.
- **Excel is for the monthly slice.** n8n writes a workbook per project on the share; you never edit it directly.
- **Agents talk to ERPNext directly** via whitelisted API methods. n8n is the routing layer, not a data store.



What you actually see at /app/pmo

Captured today against the live site (<https://vimitconverters.frappe.cloud/app/pmo>) using a Playwright headless browser with API-token auth. These are the screens you sign in to.

The screenshot shows the 'Portfolio · Inbox' view of the VCL PMO application. The interface includes a sidebar with navigation options like 'VCL PMO Doctype', 'Search', 'Notification', 'PMO Sync Log', 'PMO Requirement', 'PMO OAT Check', and 'VCL PMO'. The main content area displays a live KPI ticker at the top with metrics for UTC, Projects, Reqs, Done, In Review, and RAID Open. Below this is a section titled 'VCL PMO' with a 'New Requirement' button and a 'Refresh' button. The 'Inbox' section lists 8 portfolio items that need attention, each with a status chip (Done, In Review, Blocked, or High) and a brief description. The items are: 03 Frappe-native PMO UI at /app/pmo with Steel+Pulse dashboard (Done), 04 n8n-managed read/write per-project Excel mirror (In Review), 07 Task/status mirror only; no financial document submission (In Review), 08 Desk navigation and PMO dashboard actions for docs, UAT, OAT and sync logs (Done), 09 PMO UAT Case and PMO OAT Check records with pass/fail evidence (Done), 10 Testing documentation, n8n sync contract, migration brief and cutover checklist (Done), 009 Hamada 01 reclassification — R2R vs S2S Printing (Blocked), and R n8n Excel mirror workstream (High).

The Inbox view — top: live KPI ticker (UTC, projects, requirements done, in review, RAID open). Below: portfolio-level requirements that need attention right now. Status chips match Brand v11 (Green = Done, Amber = In Review, Sage / Blue = brand accents).

Inbox should not be the first page? Or only show items pending approval.

V VCL PMO Doctype
tanuj.haria@vimit....

Q Search Ctrl+K

🔔 Notification

☰ PMO Sync Log

☰ PMO Requirement

☰ PMO OAT Check

📁 VCL PMO

🏠 / VCL PMO

LIVE UTC 15:57:32 PROJECTS 2 REQS 23 DONE 16 IN REVIEW 2 RAID OPEN 1

VCL PMO
Portfolio, project workspace, test history, RAID, and documentation

New Requirement Refresh

Inbox Projects Roadmap RAID Documentation Test Status

Projects
Click a project card to open its workspace

VCL PMO System
VCL - DEV - PMO - 002
Frappe-native PMO + n8n Excel mirror
In Build Critical

Production Log & Job Card System
VCL - DEV - PROD - 001
ERPNext v16 (Frappe Cloud) — production_log Frappe app
In Build High

TH Tanuj Haria
tanuj.haria@vimit.com

Two projects currently live: VCL PMO System (this one) and Production Log & Job Card System. Progress bars + status chips. Click a card to drop into the project workspace.



Inside the project workspace

Clicking the project card opens its full workspace: 13 sub-tabs across the top, project meta on the side panel, breadcrumb navigation. This is where plans get written and shifts get allocated.

The screenshot displays the 'VCL PMO System · Overview' workspace. The top navigation bar includes a user profile 'VCL PMO Doctype' and a breadcrumb '/app/pmo#p/VCL-DEV-PMO-002'. A status bar shows 'LIVE UTC 15:57:34' and project metrics: 'PROJECTS 2', 'REQS 23', 'DONE 16', 'IN REVIEW 2', and 'RAID OPEN 1'. The left sidebar contains a search bar, a notification bell, and a list of project management tools: 'PMO Sync Log', 'PMO Requirement', 'PMO OAT Check', and 'VCL PMO'. The main content area features a 'VCL PMO' header with a 'New Requirement' button and a 'Refresh' button. Below this is a tabbed interface with 'Overview' selected, followed by 'Portfolio', 'Timeline', 'Open Items', 'Plans', 'Shifts', 'Milestones', 'RAID', 'UAT', 'OAT', 'Test History', 'Documentation', and 'Activity'. The 'Overview' tab shows the 'VCL PMO System' title, a description 'Build the Frappe-native project management system for VCL development work. Excel remains a mirror through n8n.', and a progress card indicating '35%' completion. To the right of the progress card are two cards: '1 Milestones' and '1 RAID items'. At the bottom, a text box provides a summary: 'Project Overview tab. Title, current phase, progress card (35%), open milestones (1), open RAID items (1). Sub-tabs: Overview · Timeline · Open Items · Plans · Shifts · Milestones · RAID · UAT · OAT · Test History · Documentation · Activity.'

? Where is the back button
How is progress Hacked?

V

VCL PMO Doctype

tanuj.haria@vimit...

🔍

Search

Ctrl+K

🔔

Notification

☰

PMO Sync Log

☰

PMO Requirement

☰

PMO OAT Check

📁

VCL PMO

/

VCL PMO

LIVE

UTC 15:57:38

PROJECTS 2

REQS 23

DONE 16

IN REVIEW 2

RAID OPEN 1

VCL PMO

Portfolio, project workspace, test history, RAID, and documentation

New Requirement

Refresh

Portfolio

> VCL-DEV-PM0-002

> Plans

> PLAN-0002

Slack Integration

Allocated - 1 proposed item

Can we work on a plan to integrate into slack.

All plans should be sent via slack into this channel: <https://vimitconverte-jfm8334.slack.com/archives/C0B5DA141MM>

In pdf format that can work well on boox air5 or remarkable

Add Item

Allocate selected to Claude

Allocate selected to Codex

Allocate selected to Human

☐	Type	Title	Description	UAT	OAT	Hint	Promoted
☐	Shift	Slack Integration	SEE THE NOTES	✓	✓	claude	PMO Shift SHIFT-0003

TH

Tanuj Haria

tanuj.haria@vimit.com

A specific plan opened: PLAN-0002 "Slack Integration" — Allocated status, 1 proposed item. Description card with the full plan text including the target Slack channel URL. Below: bulk-action buttons (Add Item, Allocate to Claude / Codex / Human) and the items table showing SHIFT-0003 promoted from this plan.




VCL Brand v1.1 – the colours we use

Every colour in this report comes from VCL Brand & Visual Identity Standards v1.1 (May 2026). Verified against the deployed `pmo.css` tokens at `/app/pmo`. No invented hexes.



Primary identity


 VCL Navy H1, document titles, cover page #1D2766	 VCL Blue Primary action, links, H2, table header #2B3990
 VCL Blue Mid Dividers, secondary icons, chart lines #5C6DBE	 VCL Blue Light Callout fills, info backgrounds #D6DBF5
 VCL Blue Pale Page tints, hover states #EEF0FB	 VCL Sage Brand accent – logo, user pill, active nav #5A9367

Status colours


 VCL Green Pricing, Complete status, positive KPIs #1B7A45	 VCL Green Light Complete row fills #D4EDE0
 VCL Amber Warnings, In Progress, AR overdue < 90d #B86B00	 VCL Amber Light Warning row fills #FFF0CC
 VCL Red RESTRICTED · errors only, 90+ day AR #C0392B	 VCL Red Light RESTRICTED · error row fills only #FADBDB

Neutrals

 Ink Body text, H3+ #1C1C1E	 Mid Grey Secondary text, captions #4A4F5C
 Muted Footnotes, metadata, helper labels #8A909E	 Rule All borders / dividers #CBD2E0

**Surface**

Alt table rows, page
tints

#F4F5F8**White**

Page background

#FFFFFF

Rules of use

- **Blue is primary.** Not navy-black. Not orange-amber. Buttons, links, table headers — all VCLBlue #2B3990.
- **Sage is the brand accent.** Logo mark, user-pill avatar, active nav indicator. NOT for status colour.
- **Green is for money + complete.** Pricing figures and "Done" — never use blue for these.
- **Amber replaces red for most warnings.** Red is restricted to system errors and 90+ day AR overdue.
- **Typography:** Manrope (UI), JetBrains Mono (IDs, code). Embedded as base64 in this PDF; no CDN.

What comes next

Before this Friday (29–30 May)

OWNER	ACTION	BY
Tanuj	Install a Slack bot in the workspace, drop its token into the PMO site settings, invite it to #ai-pmo-plans . <i>use #vcl-ai-pmo-plans</i>	29 May
Tanuj	Walk the back-button fix on three real flows (Plans → Plan, Shifts → Shift, UAT case detail). Sign off SHIFT-0001. <i>- ? how?</i>	29 May
Tanuj	Once the bot is in: click Send PDF to Slack on one plan. Confirm it lands and reads cleanly on reMarkable. Sign off SHIFT-0003. <i>?</i>	29 May
Codex	Write the spec for "auto-review of new plans" — six points, no code. Lands as a markdown doc in the repo.	30 May

Following week (2–7 June)

OWNER	ACTION	BY
Tanuj	Review the auto-review spec, mark it Pass, hand off to Claude or Codex to build.	2 Jun
Tanuj	Close the Phase 2 Foundation milestone (MS-PMO-001). System officially the master for development work.	3 Jun
Claude or Codex	Build the scheduled plan-review job (nightly sweep, capacity-aware routing, single approve action).	5 Jun
Tanuj	UAT the scheduled job end-to-end. Mark project Done.	7 Jun

Open questions for Tanuj

Q1. Slack bot — new *VCL PMO Bot* or reuse an existing workspace bot? (Recommend new, scopes stay minimal.) *use existing*

Q2. Auto-review trigger — every 6 hours, nightly at 23:00, or hourly when an unallocated plan appears? (Recommend nightly 23:00.) *- TBC*

Q3. Capacity probe for Codex — manual flag in site settings, or external monitor file? (Recommend manual flag this round.) *manual*

Q4. Where do approvals live — Slack with a button, Telegram with a reply, or just the Plans tab?
(Recommend Slack permalink back to /app/pmo.)



Tanuj Haria — Sponsor



Date

