

VCL PMO System

A single, plain-English status pack for the project we are using to build the system that runs all our other projects.

PROJECT ID	SPONSOR	PHASE
VCL-DEV-PMO-002	Tanuj Haria	Phase 2 – Build
STARTED	TARGET FINISH	THIS REPORT
27 May 2026	7 June 2026	28 May 2026

Where we are today

Status as at 21:30 EAT, 28 May 2026.

DONE

2

work blocks shipped

IN FLIGHT

1

waiting on one
setup step

WAITING

1

design write-up
pending

HEALTH

On track

target 7 Jun stands

One sentence: The PMO is being built inside ERPNext as the new home for all VCL development work – so plans, tasks, agents, testing and approvals all live in one place. As of today, four of the four planned work blocks are either shipped or coded; the only remaining steps before the system is end-to-end operational are one Slack token install and one design write-up.

What we just finished

WHAT	WHY IT MATTERS	STATUS
Back button works everywhere	Pressing browser Back from any sub-page now returns to the right tab instead of landing on a "page not available" error. Reload and pasted links also work.	• DONE
Tests grouped by what they test	Instead of one long flat list of UAT/OAT items, each shift's tests sit under a clear header showing pass/fail/blocked counts. Easier to walk through, easier to sign off.	• DONE

Built but waiting on one setup step

WHAT	WHY IT MATTERS	WHAT IT NEEDS
Plans go to Slack as PDFs	One click renders any plan as a clean, A4, VCL-branded PDF and drops it in #ai-pmo-plans. Sized for reMarkable / Boox.	Install a Slack bot token in the site settings, invite the bot to the channel. About 10 minutes of admin.

Still on the drawing board

WHAT	WHY IT MATTERS	OWNER
Auto-review of new plans by agents	Today every new plan needs Tanuj to manually choose Claude / Codex / human per item. The design will let an agent draft the proposed allocation overnight and send Tanuj a single Approve button.	Codex — design only, by 30 May



How it works – the buttons in order

Two lanes: plan-level (four buttons, independent) and shift-level (per-shift after allocation). Blue = primary action; amber = brand action; outline = secondary.

PLAN-LEVEL – ONE PLAN, FOUR BUTTONS (INDEPENDENT)

01 Open /app/pmo and pick the project

VCLPMO System

Lands on the project page with all the tabs across the top.

02 Plans tab – start a new plan

+ New Plan

Modal opens. You type a title + description, click Save.

03 Add items + send the brief to Slack (independent of allocation)

+ Add Item

Send PDF to Slack

Add Item builds the proposed-item list. Send PDF renders the plan and posts it to #ai-pmo-plans – does NOT change the plan's status.

04 Tick items + allocate to an agent or human (the act of allocating IS the approval)

Allocate to Claude

Allocate to Codex

Allocate to Human

Items become Shifts. Each Shift auto-creates UAT/OAT records, bucketed under the shift.

SHIFT-LEVEL – PER-SHIFT AFTER ALLOCATION

05 On each shift row, dispatch the work

Execute via n8n

Start

Complete

Block

Execute via n8n posts to the webhook → agent runs → calls Complete back into ERPNext, which logs the UAT/OAT runs.

Figure 1. Plan-level vs shift-level – the four plan-level buttons act on a plan but don't change its status; the act of allocating IS the approval. The shift-level row only appears once items become shifts.

Then the agent loop fires

Once a shift is dispatched, the rest of the cycle runs without you. Each lane is one actor; arrows show the handover.

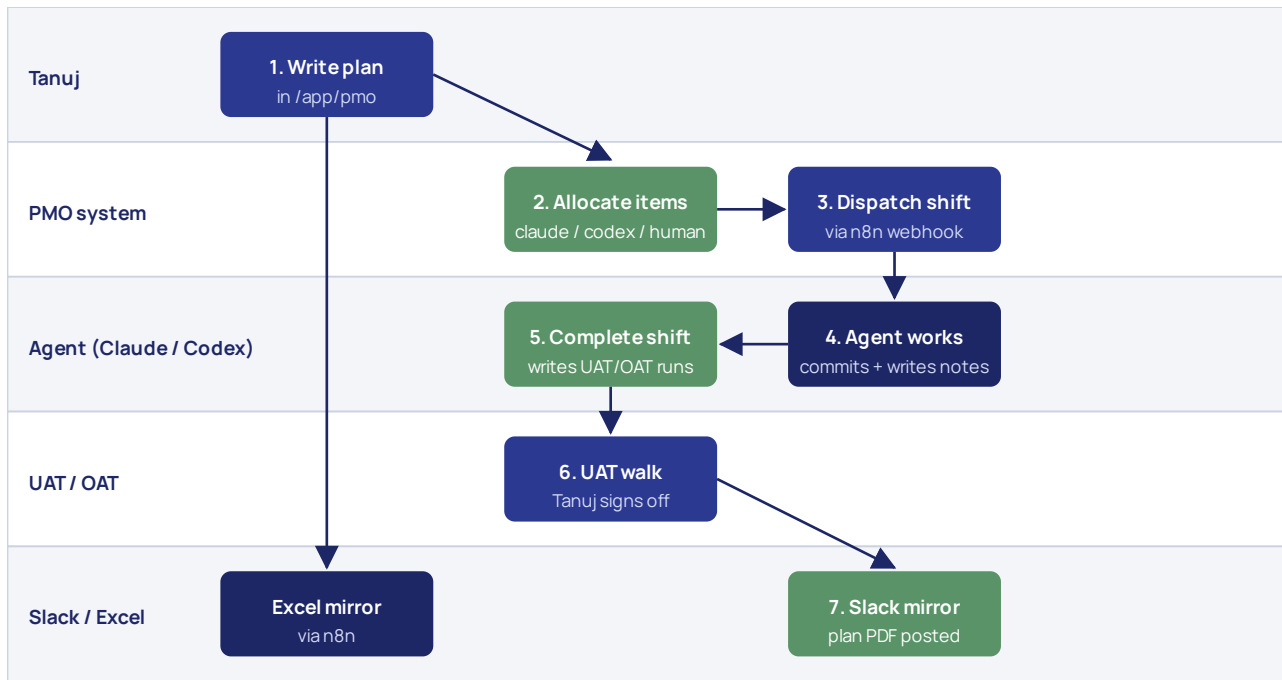


Figure 2. One full loop from plan to signed-off tests, mirrored to Slack and Excel.



The auto plan-review loop

Direct from Tanuj's hand-written page-4 annotation on the v4 review. This is the design SHIFT-0002 (Codex) is now writing up as a spec.

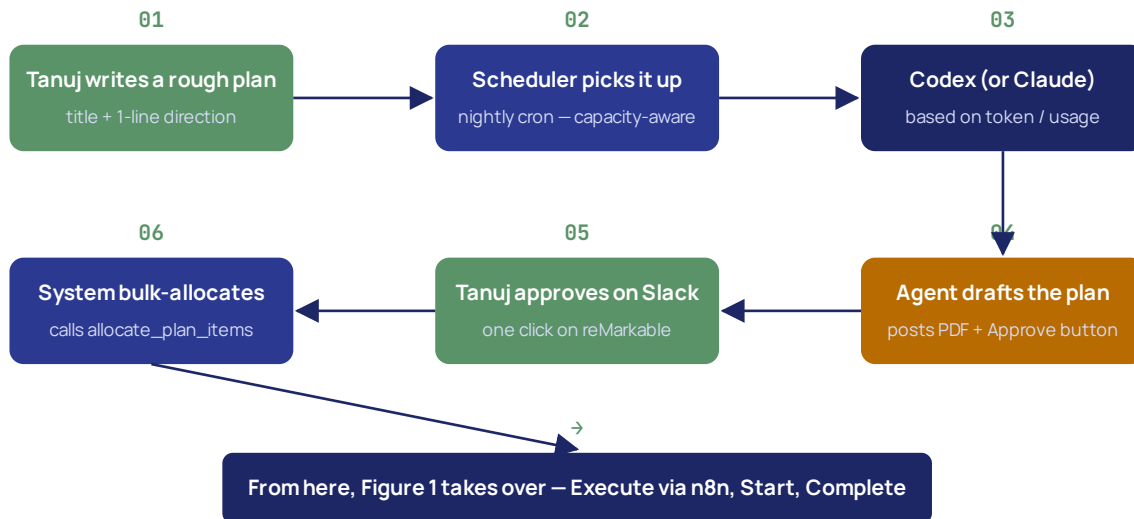


Figure 3. The six-step auto-review loop. Tanuj's rough plan → agent drafts → Slack approval → bulk-allocate. After step 6, control returns to Figure 1 (Execute via n8n → Start → Complete).

What changes in /app/pmo

- **Inbox becomes the queue.** The Inbox tab gets filtered to "needs Tanuj" — plans waiting for approval, shifts waiting for UAT sign-off, blocked requirements. Today it shows too much.
- **New Plan stays the entry point.** Tanuj writes a one-line direction in /app/pmo (same modal as today) — no need to leave for Slack.
- **The agent drafts.** Codex (default) or Claude (fallback when Codex is at quota) reads the rough plan + project context + the last 5 approved plans on the same project, expands the items, hints assignees.
- **The PDF lands in Slack.** Same Send PDF to Slack button — but now with an "Approve all to Claude / Codex / Human" Block-Kit button below the file.
- **One click bulk-allocates.** The button calls `slack_approve_plan(plan_id, allocate_to)` which delegates to the existing `allocate_plan_items` and stamps `approved_by` + `approved_at`.

What stays the same

- You can still allocate manually in /app/pmo whenever you want. The auto-loop is an option, not a replacement.
- Execute via n8n + Complete are unchanged.
- UAT/OAT records auto-create on allocation, same as today.

Your review questions, answered

All seven annotations from the v4 reMarkable review (archived at [briefs/review/2026-05-28_status_report_v4_annotated.pdf](#)).

Q1. How do we install the Slack bot? See the separate one-page setup card (VCL-PMO_slack_bot_setup_card.pdf). Five steps: create app → add chat:write + files:write scopes → install → invite to #ai-pmo-plans → drop the xoxb-... token into Frappe Cloud's site_config via bench set-config. About 10 minutes.

Q2. What about new projects? Today the SPA has no "New Project" button — you have to use the bare Desk form at /app/pmo-project/new. Codex is adding a + New Project button to the portfolio toolbar (next to "New Requirement"), wired to a new create_project API. Codex Item B in the review-response brief.

Q3. Who approves new plans? Today: nothing. A new Plan sits at status=Draft until you click "Allocate selected to ..." — the act of allocating IS the approval. Auto-review (Figure 3 above, SHIFT-0002) introduces a Slack-based approval button so you can approve without opening /app/pmo.

Q4. How are Send PDF / Allocate / Execute via n8n linked? They're not — they're independent. **Send PDF** renders + posts and does NOT change plan state. **Allocate** promotes ticked items into Shifts (status = Allocated). **Execute via n8n** is per-shift, fires the agent webhook. Figure 1 on page 3 has been split into plan-level vs shift-level lanes to make this obvious.

Q5. What does the agent do, and how does it fire up? (1) dispatch_shift(shift_id) reads pmo_n8n_dispatch_url from site_config; (2) POSTs the shift payload to n8n; (3) n8n routes by assigned_to (claude / codex) — currently designed to trigger a CLI runner on the dev machine; (4) the agent works, commits, then POSTs back to /api/method/.../complete_shift with output notes + UAT/OAT results; (5) ERPNext flips status → Done, stamps actual_end, logs the UAT/OAT runs. The n8n routing layer is the gap to close.

Q6. The plan-review flow you sketched. That's SHIFT-0002 — Codex's allocated planning shift. Captured exactly as you wrote it, drawn as Figure 3 above. Codex is finishing the spec (briefs/2026-05-28_SCHEDULED_PLAN_REVIEW_SPEC.md) covering: scheduler trigger, capacity probe (pmo_codex_available site_config flag), reviewer payload, Slack-Block-Kit approval surface, action on approve, failure modes.

Q7. Inbox first-page UX. Agreed — Inbox is too noisy. Codex is filtering Inbox to "needs Tanuj" only: plans waiting for allocation, shifts waiting for UAT sign-off, blocked requirements, plan reviews pending (once SHIFT-0002 ships). Codex Item C in the review-response brief.

Where the work is now

OWNER	ITEM	STATUS
Claude	This v5 status report — incorporates all 7 answers, adds Figure 3 (auto-review), splits Figure 1 lanes.	• DONE
Claude	Slack bot setup card (one-page A4).	• DONE
Codex	SHIFT-0002 spec from Tanuj's page-4 flow (Item A).	• ASSIGNED
Codex	+ New Project button on portfolio toolbar (Item B).	• ASSIGNED
Codex	Inbox filter — "needs Tanuj" only (Item C).	• ASSIGNED
Tanuj	Install Slack bot per the setup card.	• READY
Tanuj	UAT walk SHIFT-0001 (back-nav fix already shipped).	• READY



Where each piece lives

We deliberately do *not* try to put everything in one tool. Two anchors: ERPNext is the operational source of truth, Slack + Excel are downstream review surfaces that already work for the team.

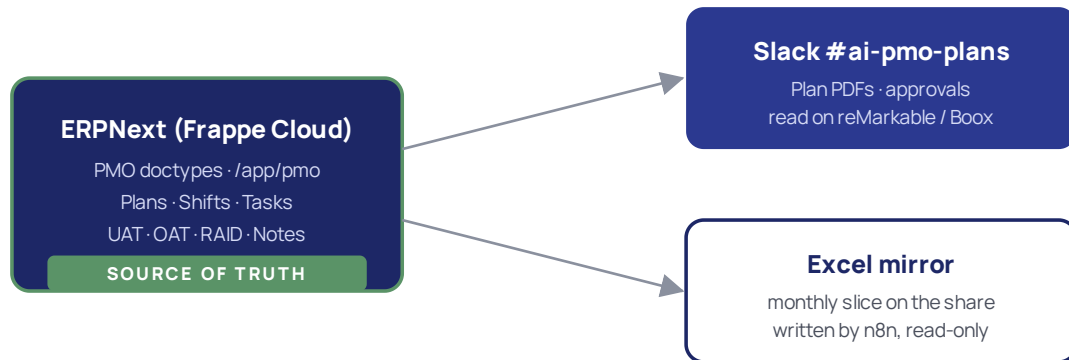


Figure 3. One source of truth, two downstream review surfaces. No reverse writes from Slack or Excel back into ERPNext.

What that means in practice

- **You edit in ERPNext.** Everything else mirrors automatically.
- **Slack is for reading and annotating.** Plans land there as PDFs; nothing in Slack writes back.
- **Excel is for the monthly slice.** n8n writes a workbook per project on the share; you never edit it directly.
- **Agents talk to ERPNext directly** via whitelisted API methods. n8n is the routing layer, not a data store.



What you actually see at /app/pmo

Captured today against the live site (<https://vimitconverters.frappe.cloud/app/pmo>) using a Playwright headless browser with API-token auth. These are the screens you sign in to.

The screenshot displays the 'Portfolio · Inbox' interface of the VCL PMO application. The top navigation bar is dark blue with the title 'Portfolio · Inbox' on the left and the path '/app/pmo' on the right. Below the navigation bar, a sidebar on the left contains a user profile for 'VCL PMO Doctype' (tanuj.haria@vimit.com) and a list of menu items: 'Search' (Ctrl+K), 'Notification', 'PMO Sync Log', 'PMO Requirement', 'PMO OAT Check', and 'VCL PMO'. The main content area features a live KPI ticker at the top showing 'LIVE UTC 15:57:31', 'PROJECTS 2', 'REQS 23', 'DONE 16', 'IN REVIEW 2', and 'RAID OPEN 1'. Below the ticker is the 'VCL PMO' header with the subtitle 'Portfolio, project workspace, test history, RAID, and documentation'. A 'New Requirement' button and a 'Refresh' button are located to the right. A tabbed interface below the header shows 'Inbox' as the active tab, with other tabs for 'Projects', 'Roadmap', 'RAID', 'Documentation', and 'Test Status'. The 'Inbox' section is titled 'Inbox' with a subtitle '8 portfolio items need attention'. It lists eight items, each with a status chip (Green for Done, Amber for In Review, Red for Blocked, Blue for High) and a 'Done' or 'In Review' button. The items are: 03 Frappe-native PMO UI at /app/pmo with Steel+Pulse dashboard (Done), 04 n8n-managed read/write per-project Excel mirror (In Review), 07 Task/status mirror only; no financial document submission (In Review), 08 Desk navigation and PMO dashboard actions for docs, UAT, OAT and sync logs (Done), 09 PMO UAT Case and PMO OAT Check records with pass/fail evidence (Done), 10 Testing documentation, n8n sync contract, migration brief and cutover checklist (Done), 009 Hamada 01 reclassification — R2R vs S2S Printing (Blocked), and R n8n Excel mirror workstream (High). The bottom of the interface shows the user profile for 'Tanuj Haria' (tanuj.haria@vimit.com).

The Inbox view — top: live KPI ticker (UTC, projects, requirements done, in review, RAID open). Below: portfolio-level requirements that need attention right now. Status chips match Brand v1.1 (Green = Done, Amber = In Review, Sage / Blue = brand accents).

V

VCL PMO Doctype

tanuj.haria@vimit....

▼

Q

Search

Ctrl+K

🔔

Notification

☰

PMO Sync Log

☰

PMO Requirement

☰

PMO OAT Check

📁

VCL PMO

🏠

/ VCL PMO

LIVE

UTC 15:57:32

PROJECTS 2

REQS 23

DONE 16

IN REVIEW 2

RAID OPEN 1

VCL PMO

Portfolio, project workspace, test history, RAID, and documentation

New Requirement

Refresh

Inbox

Projects

Roadmap

RAID

Documentation

Test Status

Projects

Click a project card to open its workspace

VCL PMO System

VCL - DEV - PMO - 002

Frappe-native PMO + n8n Excel mirror

In Build

Critical

Production Log & Job Card System

VCL - DEV - PROD - 001

ERPNext v16 (Frappe Cloud) — production_log Frappe app

In Build

High

TH

Tanuj Haria

tanuj.haria@vimit.com

Two projects currently live: VCL PMO System (this one) and Production Log & Job Card System. Progress bars + status chips. Click a card to drop into the project workspace.

VCL PMO · VCL-DEV-PMO-002 · 28 May 2026

Inside the project workspace

Clicking the project card opens its full workspace: 13 sub-tabs across the top, project meta on the side panel, breadcrumb navigation. This is where plans get written and shifts get allocated.

VCL PMO System · Overview

/app/pmo#p/VCL-DEV-PMO-002

V VCL PMO Doctype
tanuj.haria@vimit...

Q Search Ctrl+K

🔔 Notification

☰ PMO Sync Log

☰ PMO Requirement

☰ PMO OAT Check

📁 VCL PMO

/ VCL PMO

LIVE UTC 15:57:34 PROJECTS 2 REQS 23 DONE 16 IN REVIEW 2 RAID OPEN 1

VCL PMO

Portfolio, project workspace, test history, RAID, and documentation

New Requirement Refresh

Portfolio Overview Timeline Open Items Plans Shifts Milestones RAID UAT OAT Test History Documentation Activity

Portfolio > VCL PMO System

VCL PMO System

Phase 2 Build · VCL-DEV-PMO-002

VCL PMO System

Build the Frappe-native project management system for VCL development work. Excel remains a mirror through n8n.

Progress

35%

1Milestones

1RAID items

TH Tanuj Haria
tanuj.haria@vimit.com

Project Overview tab. Title, current phase, progress card (35%), open milestones (1), open RAID items (1).
Sub-tabs: Overview · Timeline · Open Items · Plans · Shifts · Milestones · RAID · UAT · OAT · Test History ·
Documentation · Activity.

V

VCL PMO Doctype

tanuj.haria@vimit...

Q

Search

Ctrl+K

🔔

Notification

☰

PMO Sync Log

☰

PMO Requirement

☰

PMO OAT Check

📁

VCL PMO

/

VCL PMO

LIVE

UTC 15:57:38

PROJECTS 2

REQS 23

DONE 16

IN REVIEW 2

RAID OPEN 1

VCL PMO

Portfolio, project workspace, test history, RAID, and documentation

New Requirement

Refresh

Portfolio

> VCL-DEV-PM0-002 > Plans > PLAN-0002

Slack Integration

Allocated - 1 proposed item

Can we work on a plan to integrate into slack.

All plans should be sent via slack into this channel: <https://vimitconverte-jfm8334.slack.com/archives/C0B5DA141MM>

In pdf format that can work well on boox air5 or remarkable

Add Item

Allocate selected to Claude

Allocate selected to Codex

Allocate selected to Human

☐	Type	Title	Description	UAT	OAT	Hint	Promoted
☐	Shift	Slack Integration	SEE THE NOTES	✓	✓	claude	PMO Shift SHIFT-0003

TH

Tanuj Haria

tanuj.haria@vimit.com

A specific plan opened: PLAN-0002 "Slack Integration" — Allocated status, 1 proposed item. Description card with the full plan text including the target Slack channel URL. Below: bulk-action buttons (Add Item, Allocate to Claude / Codex / Human) and the items table showing SHIFT-0003 promoted from this plan.




VCL Brand v1.1 – the colours we use

Every colour in this report comes from VCL Brand & Visual Identity Standards v1.1 (May 2026). Verified against the deployed `pmo.css` tokens at `/app/pmo`. No invented hexes.



Primary identity


 VCL Navy H1, document titles, cover page #1D2766	 VCL Blue Primary action, links, H2, table header #2B3990
 VCL Blue Mid Dividers, secondary icons, chart lines #5C6DBE	 VCL Blue Light Callout fills, info backgrounds #D6DBF5
 VCL Blue Pale Page tints, hover states #EEF0FB	 VCL Sage Brand accent – logo, user pill, active nav #5A9367

Status colours


 VCL Green Pricing, Complete status, positive KPIs #1B7A45	 VCL Green Light Complete row fills #D4EDE0
 VCL Amber Warnings, In Progress, AR overdue < 90d #B86B00	 VCL Amber Light Warning row fills #FFF0CC
 VCL Red RESTRICTED · errors only, 90+ day AR #C0392B	 VCL Red Light RESTRICTED · error row fills only #FADBDB

Neutrals

 Ink Body text, H3+ #1C1C1E	 Mid Grey Secondary text, captions #4A4F5C
 Muted Footnotes, metadata, helper labels #8A909E	 Rule All borders / dividers #CBD2E0

**Surface**

Alt table rows, page
tints

#F4F5F8**White**

Page background

#FFFFFF

Rules of use

- **Blue is primary.** Not navy-black. Not orange-amber. Buttons, links, table headers — all VCLBlue #2B3990.
- **Sage is the brand accent.** Logo mark, user-pill avatar, active nav indicator. NOT for status colour.
- **Green is for money + complete.** Pricing figures and "Done" — never use blue for these.
- **Amber replaces red for most warnings.** Red is restricted to system errors and 90+ day AR overdue.
- **Typography:** Manrope (UI), JetBrains Mono (IDs, code). Embedded as base64 in this PDF; no CDN.

What comes next

Before this Friday (29–30 May)

OWNER	ACTION	BY
<i>Tanuj</i>	Install a Slack bot in the workspace, drop its token into the PMO site settings, invite it to #ai-pmo-plans .	29 May
<i>Tanuj</i>	Walk the back-button fix on three real flows (Plans → Plan, Shifts → Shift, UAT case detail). Sign off SHIFT-0001.	29 May
<i>Tanuj</i>	Once the bot is in: click Send PDF to Slack on one plan. Confirm it lands and reads cleanly on reMarkable. Sign off SHIFT-0003.	29 May
<i>Codex</i>	Write the spec for "auto-review of new plans" — six points, no code. Lands as a markdown doc in the repo.	30 May

Following week (2–7 June)

OWNER	ACTION	BY
<i>Tanuj</i>	Review the auto-review spec, mark it Pass, hand off to Claude or Codex to build.	2 Jun
<i>Tanuj</i>	Close the Phase 2 Foundation milestone (MS-PMO-001). System officially the master for development work.	3 Jun
<i>Claude or Codex</i>	Build the scheduled plan-review job (nightly sweep, capacity-aware routing, single approve action).	5 Jun
<i>Tanuj</i>	UAT the scheduled job end-to-end. Mark project Done.	7 Jun

Open questions for Tanuj

Q1. Slack bot — new *VCLPMO Bot* or reuse an existing workspace bot? (Recommend new, scopes stay minimal.)

Q2. Auto-review trigger — every 6 hours, nightly at 23:00, or hourly when an unallocated plan appears? (Recommend nightly 23:00.)

Q3. Capacity probe for Codex — manual flag in site settings, or external monitor file? (Recommend manual flag this round.)

Q4. Where do approvals live — Slack with a button, Telegram with a reply, or just the Plans tab?
(Recommend Slack permalink back to /app/pmo.)

Tanuj Haria — Sponsor

Date

